


		Name	Duration	Start	Finish	Predecessors
1		Week 1	7.125 days?	10/3/23 8:00 AM	10/10/23 9:00 AM	
2		Review of project requirements / diagrams	7 days	10/3/23 8:00 AM	10/9/23 5:00 PM	
3		Backend tech selection	1 day?	10/3/23 8:00 AM	10/3/23 5:00 PM	
4		Frontend tech selection	1 day?	10/3/23 8:00 AM	10/3/23 5:00 PM	
5		Database tech selection	7 days	10/3/23 9:00 AM	10/10/23 9:00 AM	
6		Services tech selection	1 day?	10/3/23 8:00 AM	10/3/23 5:00 PM	
7		Weekly progress report	1 day	10/3/23 8:00 AM	10/3/23 5:00 PM	
8		Week 2	7 days?	10/10/23 8:00 AM	10/16/23 5:00 PM	
9		Designing file structure outlines	2 days	10/10/23 8:00 AM	10/11/23 5:00 PM	
10		Signup Page	5 days	10/12/23 8:00 AM	10/16/23 5:00 PM	9
11		Login Page	5 days	10/12/23 8:00 AM	10/16/23 5:00 PM	9
12		Creating User Models	2 days	10/13/23 8:00 AM	10/14/23 5:00 PM	18
13		Signup Page GET API	2 days	10/15/23 8:00 AM	10/16/23 5:00 PM	12
14		Signup Page POST API	2 days	10/15/23 8:00 AM	10/16/23 5:00 PM	12
15		Login Page GET API	2 days	10/15/23 8:00 AM	10/16/23 5:00 PM	12
16		Login Page POST API	2 days	10/15/23 8:00 AM	10/16/23 5:00 PM	12
17		Deciding and setting up development, testing, ...	1 day	10/10/23 8:00 AM	10/10/23 5:00 PM	
18		Defining authentication mechanisms	2 days	10/11/23 8:00 AM	10/12/23 5:00 PM	17
19		Weekly progress report	1 day?	10/10/23 8:00 AM	10/10/23 5:00 PM	
20		User Class Implementation	3 days	10/10/23 8:00 AM	10/12/23 5:00 PM	
21		Guest Class Implementation	4 days	10/13/23 8:00 AM	10/16/23 5:00 PM	20
22		Basic User Class Implementation	3 days	10/14/23 8:00 AM	10/16/23 5:00 PM	20;23
23		Account Class Implementation	4 days	10/10/23 8:00 AM	10/13/23 5:00 PM	
24		Week 3	7 days?	10/17/23 8:00 AM	10/23/23 5:00 PM	
25		Profile page	7 days	10/17/23 8:00 AM	10/23/23 5:00 PM	9
26		Home page	7 days	10/17/23 8:00 AM	10/23/23 5:00 PM	9
27		Profile page GET API	7 days	10/17/23 8:00 AM	10/23/23 5:00 PM	
28		Home page GET API	7 days	10/17/23 8:00 AM	10/23/23 5:00 PM	
29		Home page POST API	7 days	10/17/23 8:00 AM	10/23/23 5:00 PM	
30		Weekly progress report	1 day?	10/17/23 8:00 AM	10/17/23 5:00 PM	

24	21 Jan 24
----	-----------

F	W	T	F	S	S	M	T	W
---	---	---	---	---	---	---	---	---

		Name	Duration	Start	Finish	Predecessors
31		Admin Class Implementation	2 days	10/17/23 8:00 AM	10/18/23 5:00 PM	22
32		Proof Class Implementation	7 days	10/17/23 8:00 AM	10/23/23 5:00 PM	
33		AnnotationText Class Implementation	4 days	10/17/23 8:00 AM	10/20/23 5:00 PM	
34		Theorem Class Implementation	7 days	10/17/23 8:00 AM	10/23/23 5:00 PM	
35		Question Class Implementation	7 days	10/17/23 8:00 AM	10/23/23 5:00 PM	
36		Annotation Class Implementation	3 days	10/21/23 8:00 AM	10/23/23 5:00 PM	33
37	 	Week 4	7 days?	10/24/23 8:00 AM	10/30/23 5:00 PM	
38	 	Revise the Requirements	7 days	10/24/23 8:00 AM	10/30/23 5:00 PM	
39		Admin panel	7 days	10/24/23 8:00 AM	10/30/23 5:00 PM	
40		Settings page	7 days	10/24/23 8:00 AM	10/30/23 5:00 PM	
41		Admin panel GET API	7 days	10/24/23 8:00 AM	10/30/23 5:00 PM	
42		Admin panel POST API	7 days	10/24/23 8:00 AM	10/30/23 5:00 PM	
43		Settings page GET API	7 days	10/24/23 8:00 AM	10/30/23 5:00 PM	
44		Settings Page POST API	7 days	10/24/23 8:00 AM	10/30/23 5:00 PM	
45		Creating Node Models	7 days	10/24/23 8:00 AM	10/30/23 5:00 PM	
46		Creating workspace models	7 days	10/24/23 8:00 AM	10/30/23 5:00 PM	
47		Deployment for Customer Milestone 1	2 days	10/29/23 8:00 AM	10/30/23 5:00 PM	
48		Weekly progress report	1 day?	10/24/23 8:00 AM	10/24/23 5:00 PM	
49		WikiTag Class Implementation	2 days	10/24/23 8:00 AM	10/25/23 5:00 PM	
50		Tag Class Implementation	2 days	10/24/23 8:00 AM	10/25/23 5:00 PM	
51		Node Class Implementation	5 days	10/26/23 8:00 AM	10/30/23 5:00 PM	32;34;35;36;49;50
52	 	Week 5	7 days?	10/31/23 8:00 AM	11/6/23 5:00 PM	
53		Node view page - Part - 1	7 days	10/31/23 8:00 AM	11/6/23 5:00 PM	
54		Workspace page - Part - 1	7 days	10/31/23 8:00 AM	11/6/23 5:00 PM	
55		Weekly progress report	1 day?	10/31/23 8:00 AM	10/31/23 5:00 PM	
56		Node View Page GET API	7 days	10/31/23 8:00 AM	11/6/23 5:00 PM	51
57		Entry Class Implementation	7 days	10/31/23 8:00 AM	11/6/23 5:00 PM	
58		Request Class Implementation	3 days	10/31/23 8:00 AM	11/2/23 5:00 PM	
59		ReviewRequest Class Implementation	4 days	11/3/23 8:00 AM	11/6/23 5:00 PM	58;61

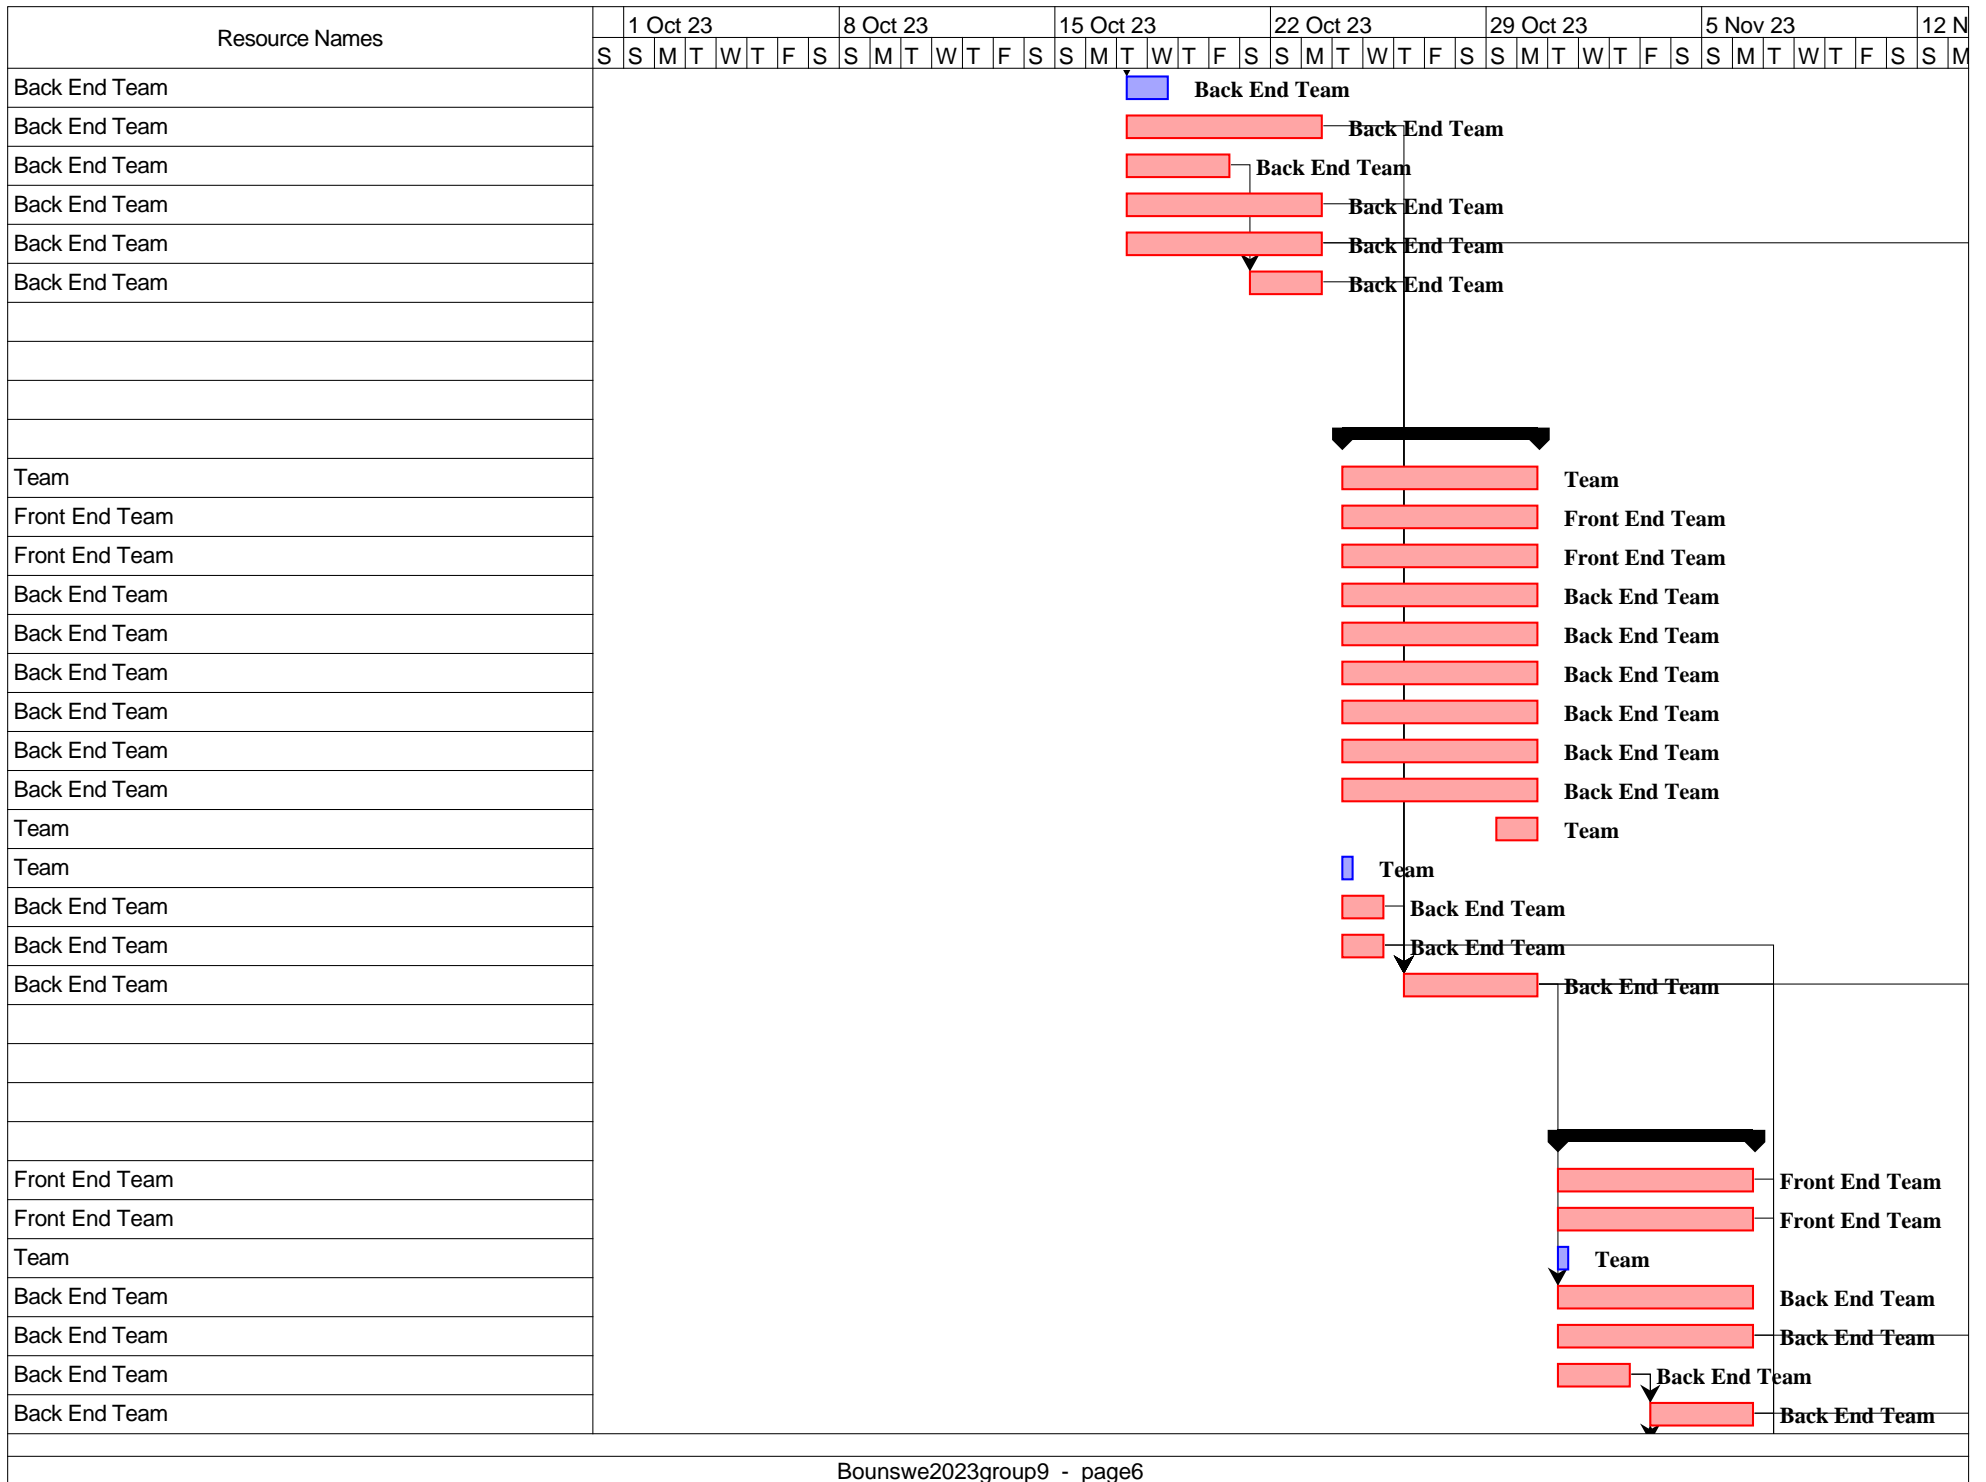

ov 23	19 Nov 23	26 Nov 23	3 Dec 23	10 Dec 23	17 Dec 23	24 Dec 23	31 Dec 23	7 Jan 24	14 Jan
T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S	S M T W T F S S M

--	--	--	--	--	--	--	--	--	--

24	21 Jan 24
----	-----------

F	W	T	F	S	S	M	T	W
---	---	---	---	---	---	---	---	---


		Name	Duration	Start	Finish	Predecessors
60		CollaborationRequest Class Implementation	3 days	11/3/23 8:00 AM	11/5/23 5:00 PM	58
61		Review Class Implementation	3 days	10/31/23 8:00 AM	11/2/23 5:00 PM	
62	 	Week 6	7 days?	11/7/23 8:00 AM	11/13/23 5:00 PM	
63		Node view page - Part - 2	7 days	11/7/23 8:00 AM	11/13/23 5:00 PM	53
64		Workspace page - Part - 2	7 days	11/7/23 8:00 AM	11/13/23 5:00 PM	54
65		Reviewer randomizer	7 days	11/7/23 8:00 AM	11/13/23 5:00 PM	
66		Weekly progress report	1 day?	11/7/23 8:00 AM	11/7/23 5:00 PM	
67		Workspace Class Implementation	7 days	11/7/23 8:00 AM	11/13/23 5:00 PM	50;51;57;59;60;61
68	 	Week 7	7 days	11/14/23 8:00 AM	11/20/23 5:00 PM	
69		Node view page Part - 3	7 days	11/14/23 8:00 AM	11/20/23 5:00 PM	63
70		Workspace page - Part - 3	7 days	11/14/23 8:00 AM	11/20/23 5:00 PM	64
71		Workspace page GET API	7 days	11/14/23 8:00 AM	11/20/23 5:00 PM	67
72		Workspace page POST API	7 days	11/14/23 8:00 AM	11/20/23 5:00 PM	67
73		Weekly progress report	1 day	11/14/23 8:00 AM	11/14/23 5:00 PM	
74		Contributor Class Implementation	7 days	11/14/23 8:00 AM	11/20/23 5:00 PM	35;51;57;60;67
75		Reviewer Class Implementation	7 days	11/14/23 8:00 AM	11/20/23 5:00 PM	59
76	 	Week 8	7 days?	11/21/23 8:00 AM	11/27/23 5:00 PM	
77		Graph page - Part 1	7 days	11/21/23 8:00 AM	11/27/23 5:00 PM	
78		Graph page GET API	7 days	11/21/23 8:00 AM	11/27/23 5:00 PM	
79		Graph page POST API	7 days	11/21/23 8:00 AM	11/27/23 5:00 PM	
80		Weekly progress report	1 day?	11/21/23 8:00 AM	11/21/23 5:00 PM	
81		Notification Class Implementation	7 days	11/21/23 8:00 AM	11/27/23 5:00 PM	
82		Search Class Implementation	7 days	11/21/23 8:00 AM	11/27/23 5:00 PM	
83		Deployment for Customer Milestone 2	2 days	11/26/23 8:00 AM	11/27/23 5:00 PM	

Resource Names	1 Oct 23					8 Oct 23					15 Oct 23					22 Oct 23					29 Oct 23					5 Nov 23					12 N																			
	S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S	M	T	W	T	F	S	S	S
Back End Team																																																		
Back End Team																																																		
Front End Team																																																		
Front End Team																																																		
Back End Team																																																		
Team																																																		
Back End Team																																																		
Front End Team																																																		
Front End Team																																																		
Back End Team																																																		
Back End Team																																																		
Team																																																		
Back End Team																																																		
Back End Team																																																		
Front End Team																																																		
Back End Team																																																		
Back End Team																																																		
Team																																																		
Back End Team																																																		
Back End Team																																																		
Team																																																		







24	21 Jan 24
----	-----------

F	W	T	F	S	S	M	T	W
---	---	---	---	---	---	---	---	---

		Name	Duration	Start	Finish	Predecessors
84		Week 9	7 days?	11/28/23 8:00 AM	12/4/23 5:00 PM	
85		Graph page - Part 3	7 days	11/28/23 8:00 AM	12/4/23 5:00 PM	77
86		Graph page GET API	7 days	11/28/23 8:00 AM	12/4/23 5:00 PM	78
87		Graph page POST API	7 days	11/28/23 8:00 AM	12/4/23 5:00 PM	79
88		Weekly progress report	1 day?	11/28/23 8:00 AM	11/28/23 5:00 PM	
89		Week 10	7 days?	12/5/23 8:00 AM	12/11/23 5:00 PM	
90		Role-related access control	7 days	12/5/23 8:00 AM	12/11/23 5:00 PM	
91		Review and Fine Tune	7 days	12/5/23 8:00 AM	12/11/23 5:00 PM	
92		Weekly progress report	1 day?	12/5/23 8:00 AM	12/5/23 5:00 PM	
93		Week 11	7 days?	12/12/23 8:00 AM	12/18/23 5:00 PM	
94		Review and Fine Tune	7 days	12/12/23 8:00 AM	12/18/23 5:00 PM	
95		Writing Privacy Policy	7 days	12/12/23 8:00 AM	12/18/23 5:00 PM	
96		Weekly progress report	1 day?	12/12/23 8:00 AM	12/12/23 5:00 PM	
97		Review and Fine Tune	7 days	12/12/23 8:00 AM	12/18/23 5:00 PM	
98		Week 12	7 days?	12/19/23 8:00 AM	12/25/23 5:00 PM	
99		Final Milestone Deployment	7 days	12/19/23 8:00 AM	12/25/23 5:00 PM	
100		Weekly progress report	1 day?	12/19/23 8:00 AM	12/19/23 5:00 PM	
101		Review and Fine Tune	7 days	12/19/23 8:00 AM	12/25/23 5:00 PM	

Resource Names	1 Oct 23					8 Oct 23					15 Oct 23					22 Oct 23					29 Oct 23					5 Nov 23					12 N														
	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	S
Front End Team																																													
Back End Team																																													
Back End Team																																													
Team																																													
Back End Team																																													
Team																																													
Team																																													
Team																																													
Team																																													
Team																																													
Team																																													
Team																																													
Team																																													
Team																																													

ov 23				19 Nov 23				26 Nov 23				3 Dec 23				10 Dec 23				17 Dec 23				24 Dec 23				31 Dec 23				7 Jan 24				14 Jan																															
T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S



24	21 Jan 24
----	-----------

F	W	T	F	S	S	M	T	W
---	---	---	---	---	---	---	---	---

--	--	--	--	--	--	--	--	--
